



工種	令和6年1月																															令和6年2月																												
	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29
準備工・調査																																																												
土地家屋調査									家屋調査 (14棟)																																																			
共通仮設									仮設水道引込																																																			
フロン・PCB									PCB検体採取 (電気室3箇所)																																																			
植栽撤去・搬出	冬期休工							植栽撤去・搬出																																																				
解体工事									A北棟 外部養生足場設置																																																			
アスベスト除去(立会)									2Fレベル1除去箇所養生																																																			
●アスベスト除去(作業)									2Fレベル1除去箇所養生																																																			
内装解体									④1F2F																																																			
									完了立会 (レベル1)																																																			
									環境確認立会 (レベル1)																																																			
									②2Fアスベスト (レベル1) 除去																																																			
									北側外壁 (レベル3) アスベスト除去																																																			
									④中央棟 東西組立																																																			
									⑤外装アスベスト完了後解体																																																			
									②1F2F																																																			

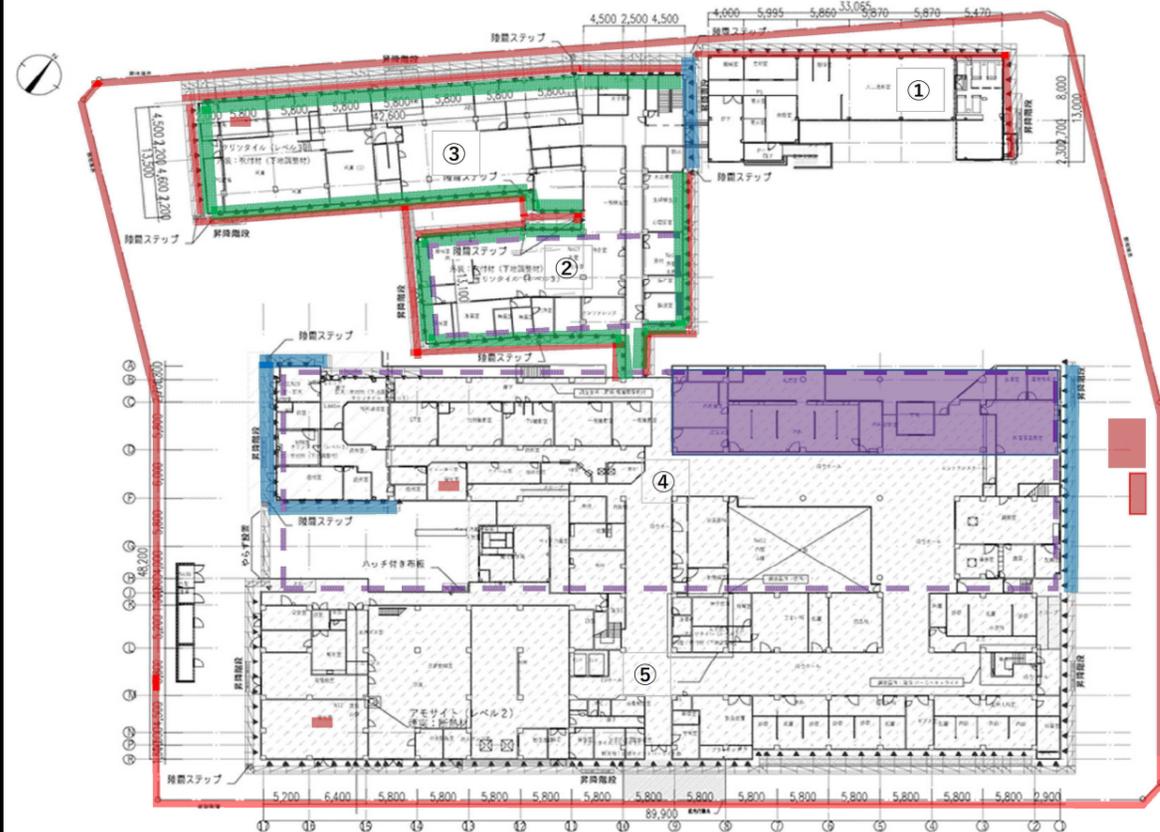

1F

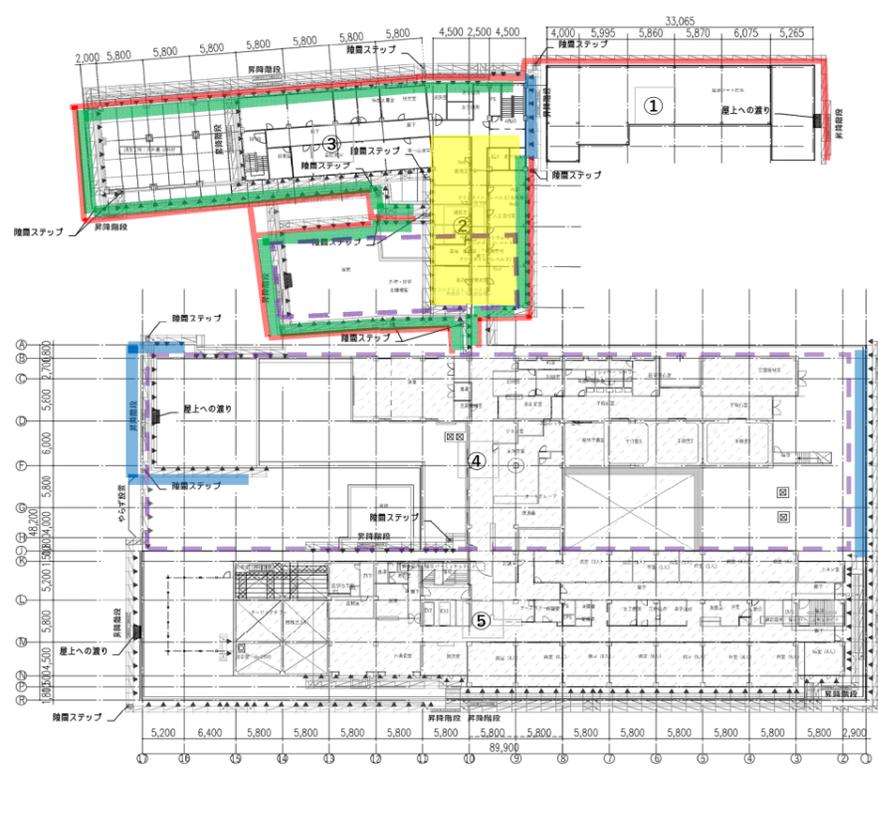

2F

記事 (立会等)	
1/18	本社・支店安全パトロール
1/26	災害防止協議会

凡例

- : 施工済 (足場 仮設事務所 仮囲い 調査)
- : 施工予定 (足場組立)
- : 施工予定 (石綿除去)
- : 施工済 (石綿除去)
- - - : 施工予定 (内装撤去)
- : 施工済 (内装撤去)

施工順序

足場：南側→北側

内装撤去：中央棟④→北側② (管理棟)

石綿除去：2F②→2F②外→2F外→1F外
